Exercise 5: Gantt Chart

FlightDeck Airport Operations System | Overall project duration: 44 days

Project days are inclusive.
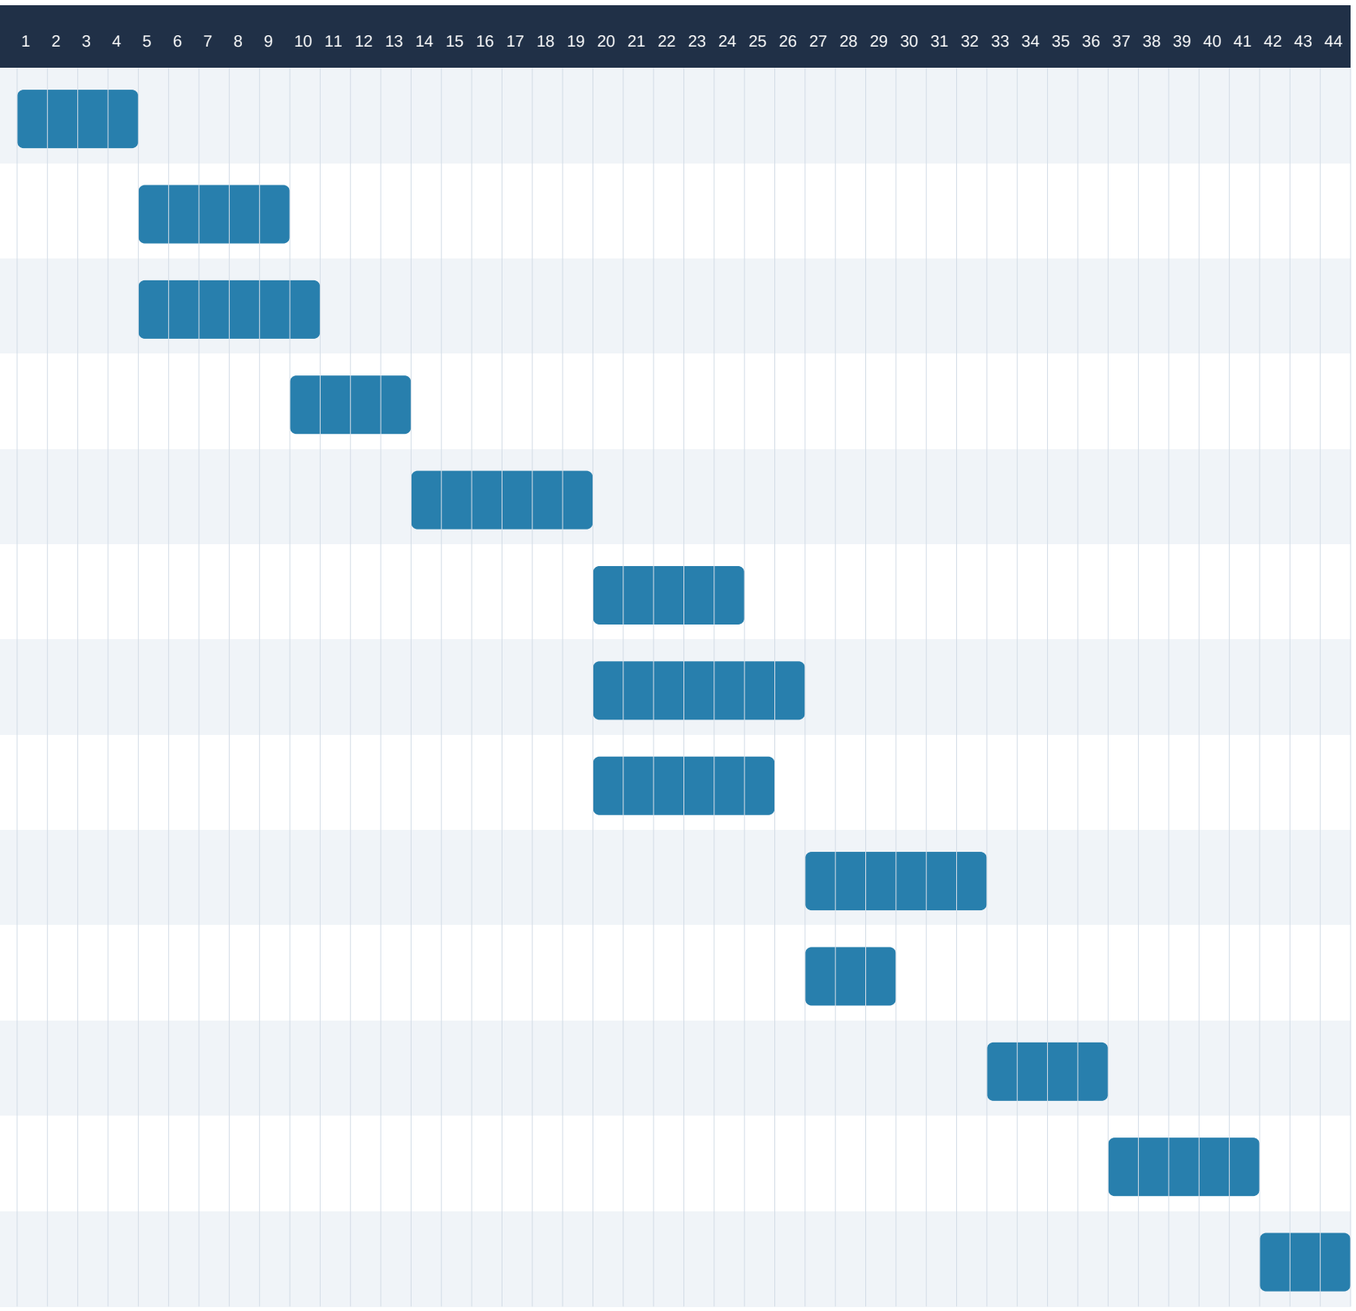
ID	Activity	Predecessors	Days	Start	Finish
T1	Requirements refinement	-	4	1	4
T2	Database design	T1	5	5	9
T3	User-interface design	T1	6	5	10
T4	Authentication and roles	T2	4	10	13
T5	Flight records module	T4	6	14	19
T6	Flight status and tower feed	T5	5	20	24
T7	Runway assignment module	T5	7	20	26
T8	Bay and occupancy module	T5	6	20	25
T9	Dashboard and flight views	T3, T6, T7, T8	6	27	32
T10	Change log module	T6, T7, T8	3	27	29
T11	System integration	T9, T10	4	33	36
T12	System testing and fixes	T11	5	37	41
T13	Deployment and documentation	T12	3	42	44
